


5. Timesheets



Total time spent: 51 hours (estimated: 48 hours). The main over-run was in user testing (+2h) and the project report (+1h). Overall, the project stayed very close to the estimated workload.

4. Timeline

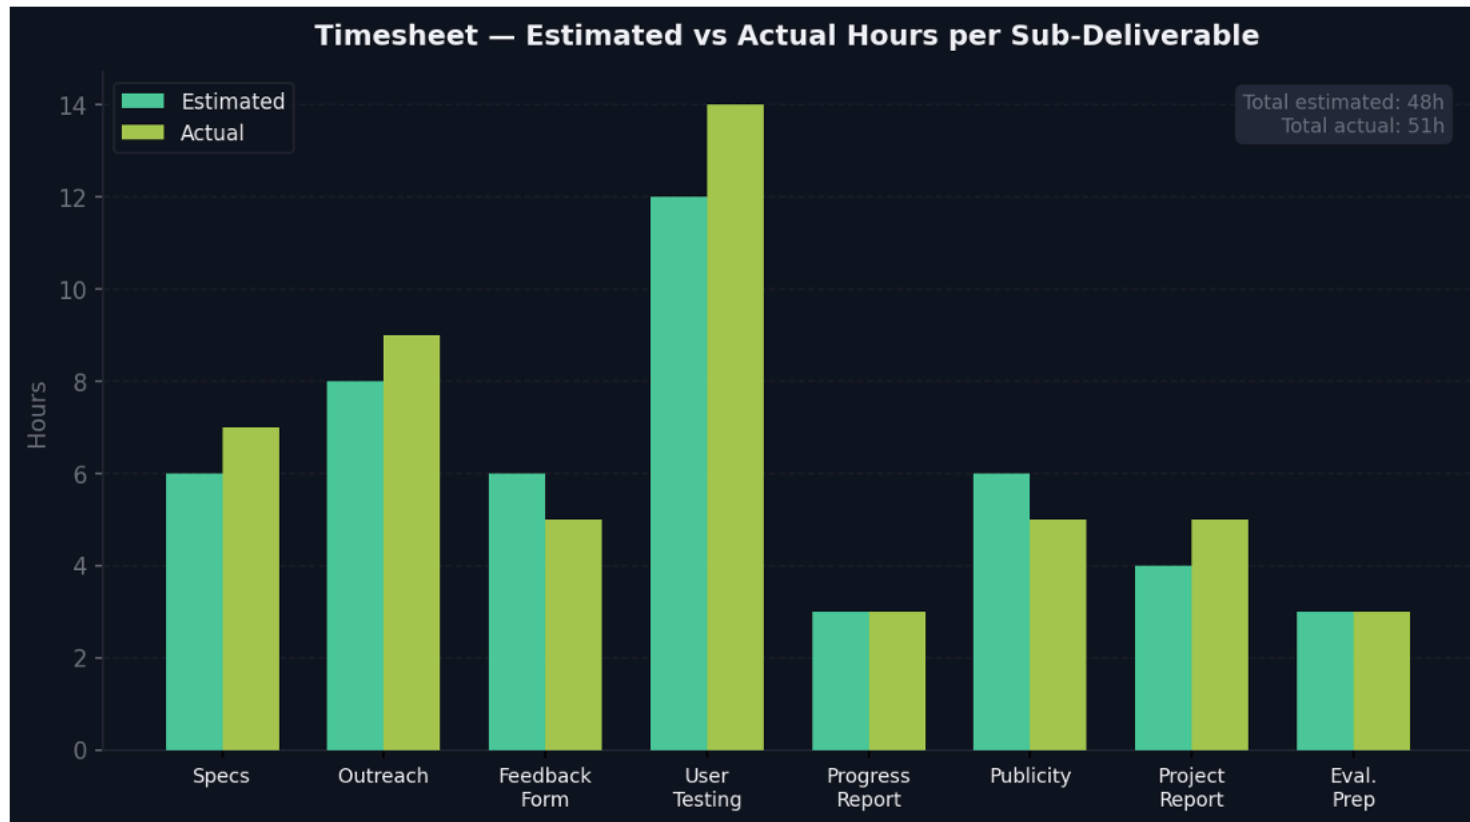

Sub-Deliverable	Planned	Actual	Responsible
1. Project Specifications	23/01/2026	25/01/2026	Hirama & Aminata
2. Outreach Article	04/02/2026	06/02/2026	Aminata & Keemyah
3. User Feedback Form	09/02/2026	11/02/2026	Aminata & Keemyah
4. User Testing (22 users)	22/02/2026	19/03/2026	All team
5. Progress Report	22/02/2026	22/02/2026	Keemyah
6. Publicity	01/03/2026	01/03/2026	Keemyah
7. Project Report	15/03/2026	19/03/2026	Hirama
8. Evaluation	23/03/2026	TBC	All team

Most sub-deliverables were delivered within 2 days of the planned date. The main delay concerned user testing, which took longer than expected due to difficulty recruiting users outside the immediate class network.
